



# **Project Overview & Scope**



## **Project Scope Remains Nearly Identical to Prior Design**

- Slight changes in the project's site elements
  - New hardscape, landscape and drop-off proposed
- 350 Seat Theater
- Black Box
- Lobby, Box Office, Front of House Support Spaces
- Support Spaces
  - Dressing Rooms
  - Scene Shop
  - Costume & Prop Storage




# **Project History**



## **Project Conception**

- This project (among many others across NMUSD) promised as part of Measure F bond in 2005.
- Measure F GO Bonds issued in 2017.
- In 2018 the board authorized the district to proceed with an RFP for design of a new 350 seat theater, and an architect was selected in 2019.
- Original project design (situated in "Site 2") was complete and approved by DSA in Late 2021.
- Initial design went out to bid, and contractor bids were received in February of 2022.
- Shortly after, District and Board began process to reevaluate theater site location.
- Held a community meeting in April of 2022 to review pros and cons of many site options of possible theater relocation.
- Board directed staff to begin process to relocate theater to "Site 3" on July 12, 2022, board meeting.

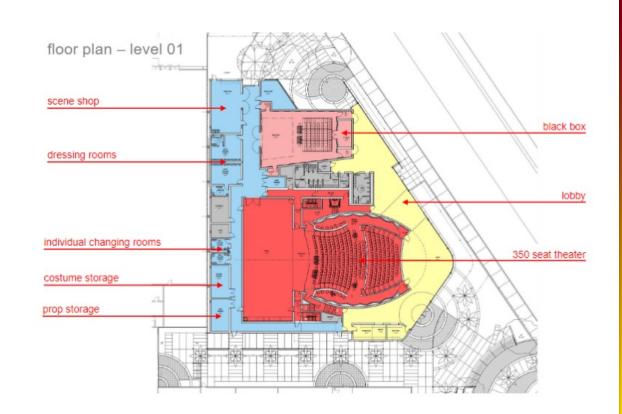




## **New Site Location**



## **Preliminary Site Plan of Theater "Location 3"**

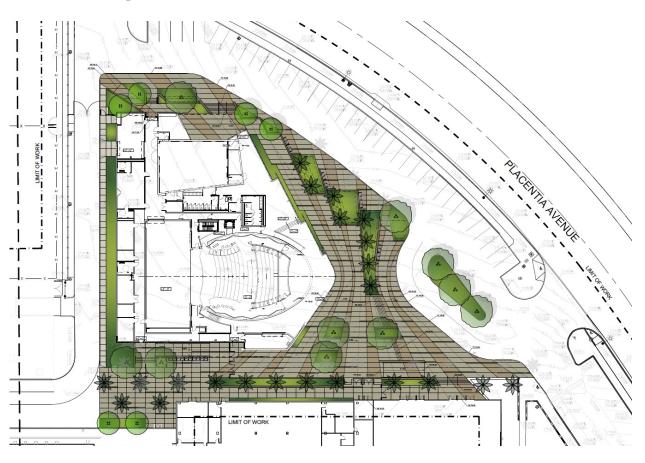

- New additional vehicular drop-off location proposed west of theater.
- Designers working to maintain as much parking as possible.
- Some building elements will require minor redesign, but the building's intent and design language are maintained from earlier designs.
- New landscape elements are proposed across the entire site.




# **New Site Location**



## **Preliminary Revised Site Renderings**



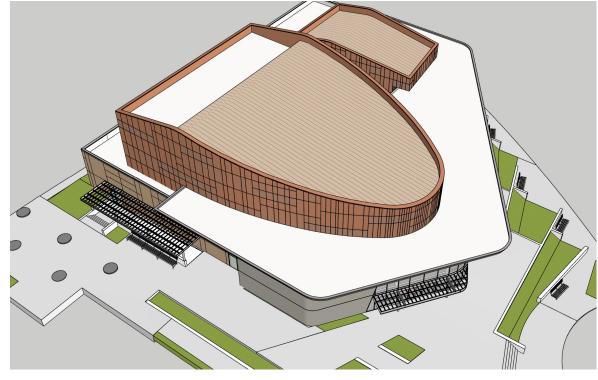




# **New Site Location**



# **Early Performance Space Renderings**



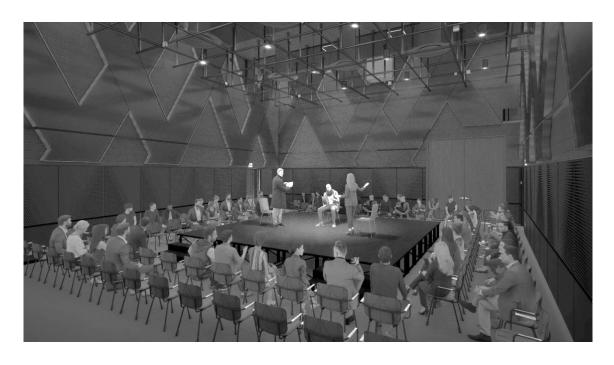



# **Project History**



## Redesign+ReBid Timeline

#### **August 2022:**

Relocation design begins.



### September 2022:

New geotechnical, underground utility, and soils investigations take place.



### September 2022:

Selection for new general contractor utilizing Lease-Lease Back delivery method begins.



#### October 2022:

Bids from interested contractors received.



### November 2022:

Proposals from contractors reviewed, and interviews with qualified firms conducted.



### November 2022:

General Contractor (Flint Builders) Board Approved.



#### December 2022:

Architect to submit redesigned building for DSA Review.



# **Project History**



### **DSA Review + Construction Timeline**

#### December 2022:

Architect to submit redesigned building for DSA Review.



#### March 2023:

DSA Review Complete



### **April 2023:**

**Construction Begins** 



#### **November 2024**

Construction Complete

